




4611 Kelly Place
Delta BC
V4K 1G8
Tel: 604-317-3786
Email: ted@phoenixroofconsultants.ca

Installation Monitoring Report

Date: May 5, 2025

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number	N/A
Address	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	Inspector	Matt	Report Number	01
		Weather	Sun/16°C	Time	1:30pm
Contractor	Flynn Canada Ltd.	Crew Size	7	Red Seal	3
				Apprentices	2

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

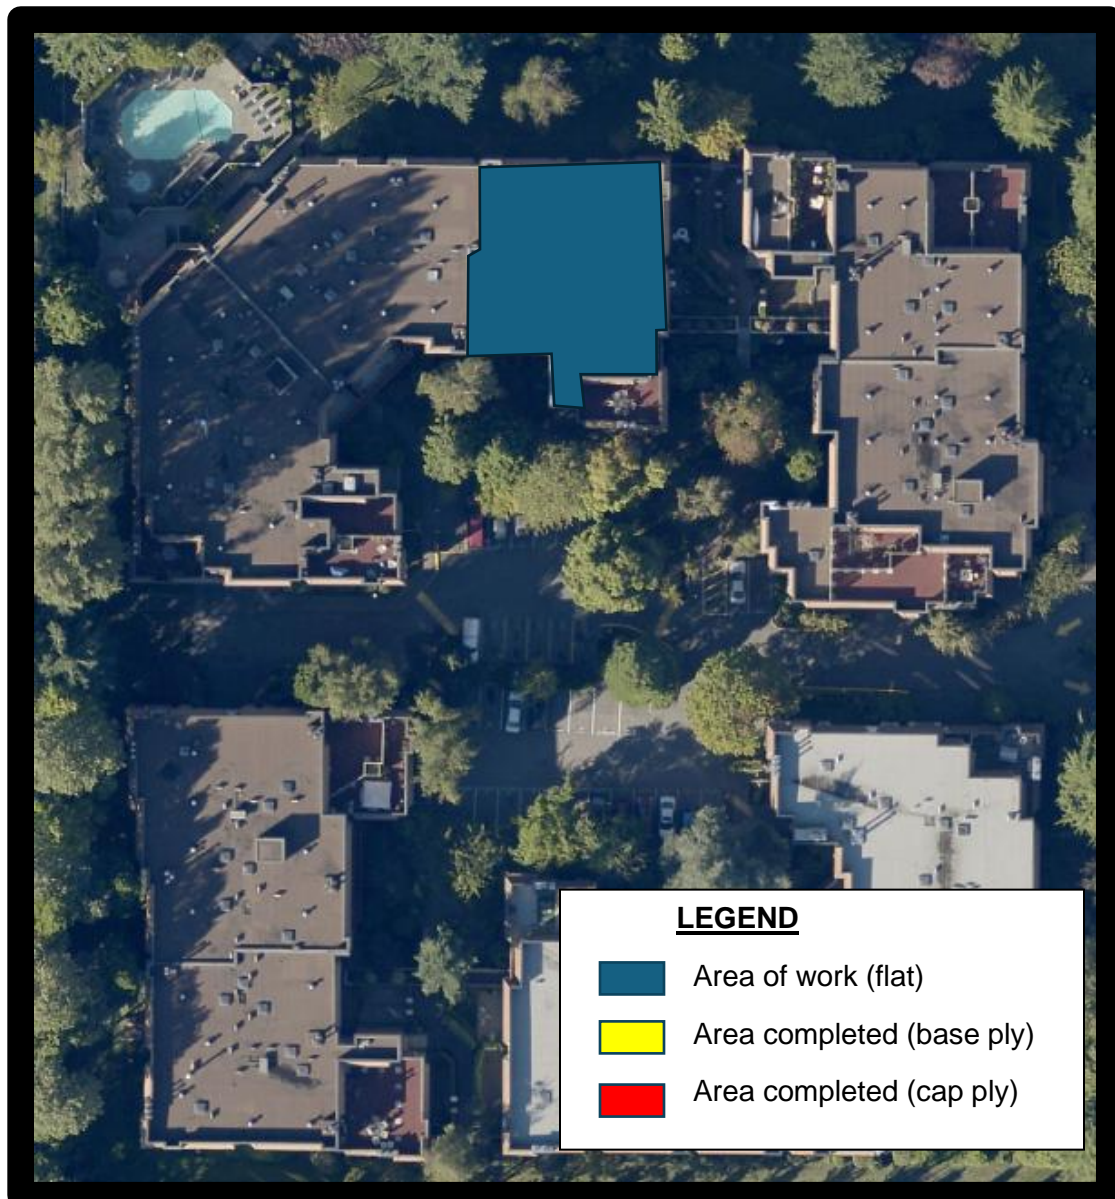

1.1 **Building B**

Scaffolding tower is set in place at the Southwest corner on noted building.



1.2 **Building B**

Crew have begun application on the Northeast corner of the noted building.





1.3 **Building B**

The specified Soprema 2 in 1 smartboard sanded with 1/2" HD is on site and being applied in place.



1.4 **Building B**

Approved manufacturers 2" barbed seam plates and #14 2" Dek fast screws are being used to secure the 2 in 1 smart p board.

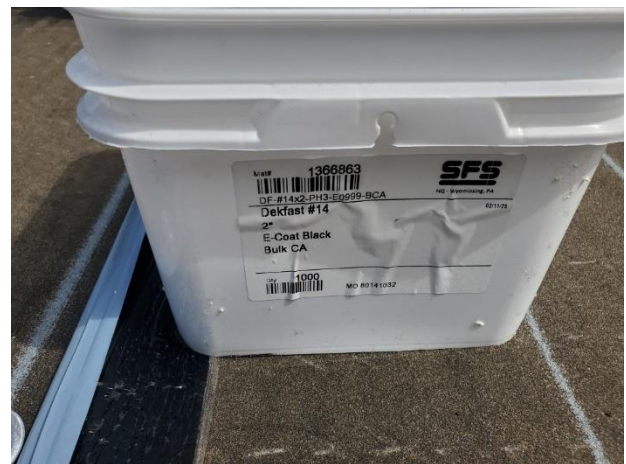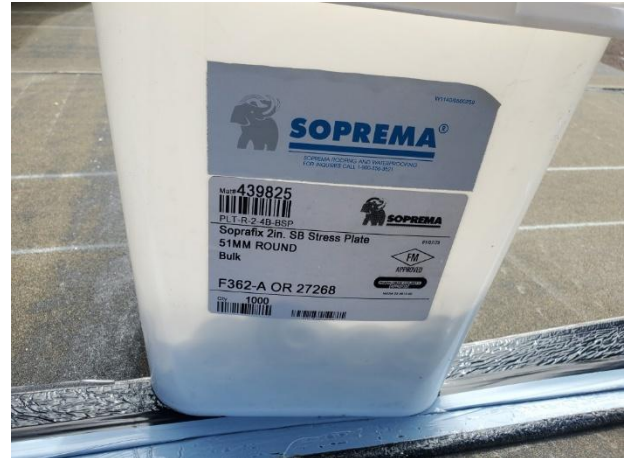

1.5 **Building B**

Sopraply Stick DUO cold applied base membrane is on site to be applied as independent base stripping and base membrane target patches at vents.



1.6 **Building B**

The 12" SopraLap stick is on site to be applied over the end joints of the 2n1 smart board. This is acceptable.



1.7 **Building B**

The membrane manufacturer approved Elastocol stick adhesive primer is on site for the base layer applications and wall details.



1.8 **Building B**

An approved high temp self-adhering membrane to be applied on the high parapet walls is on site.



1.9 **Building B**

The 3" copper spun bowl drains with integral clamping rings are on site to be installed at drain sump locations.



1.10 **Building B**

Approved roofing components and protrusion flashing are on site to be applied.



1.11 **Building B**

The roofing contractor is cutting out blisters and checking locations for deterioration.




1.12 **Building B**

The Soprema 2 in 1 smartboard sanded is being laid out in a uniform manner. Seams and end lap cover strips remain detailed.



1.13 **Building B**

Screw and plate placement, found meeting the wind-up lift calculations.

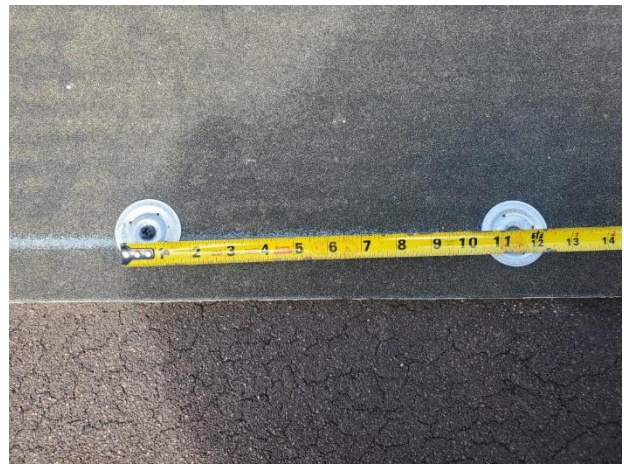

1.14 **Building B**

Membrane has begun to be removed from the base and sides of skylight curbs as per spec.



1.15 **Building B**

Vent curb details remain to be removed and detailed as per specifications.



1.16 **Building B**

Fire wall detail discussed with foreman.



Outstanding Items:

- None currently.

Reported by:

A handwritten signature in black ink, appearing to read 'Matthew Blackstock', with a stylized flourish at the end.

Matthew Blackstock, RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
