




4611 Kelly Place  
Delta BC  
V4K 1G8  
Tel: 604-317-3786  
Email: ted@phoenixroofconsultants.ca

## Installation Monitoring Report

Date: July 11, 2025

<b>Project</b>	NW 2050 Cypress Point	<b>Job Number</b>	24064	<b>RGC Number</b>	53216
<b>Address</b>	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	<b>Inspector</b>	Matthew	<b>Report Number</b>	24
		<b>Weather</b>	Sun / 27°C	<b>Time</b>	2:30pm
<b>Contractor</b>	Flynn Canada Ltd.	<b>Crew Size</b>	22	<b>Red Seal</b>	6
				<b>Apprentices</b>	13

**Distribution List:** keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

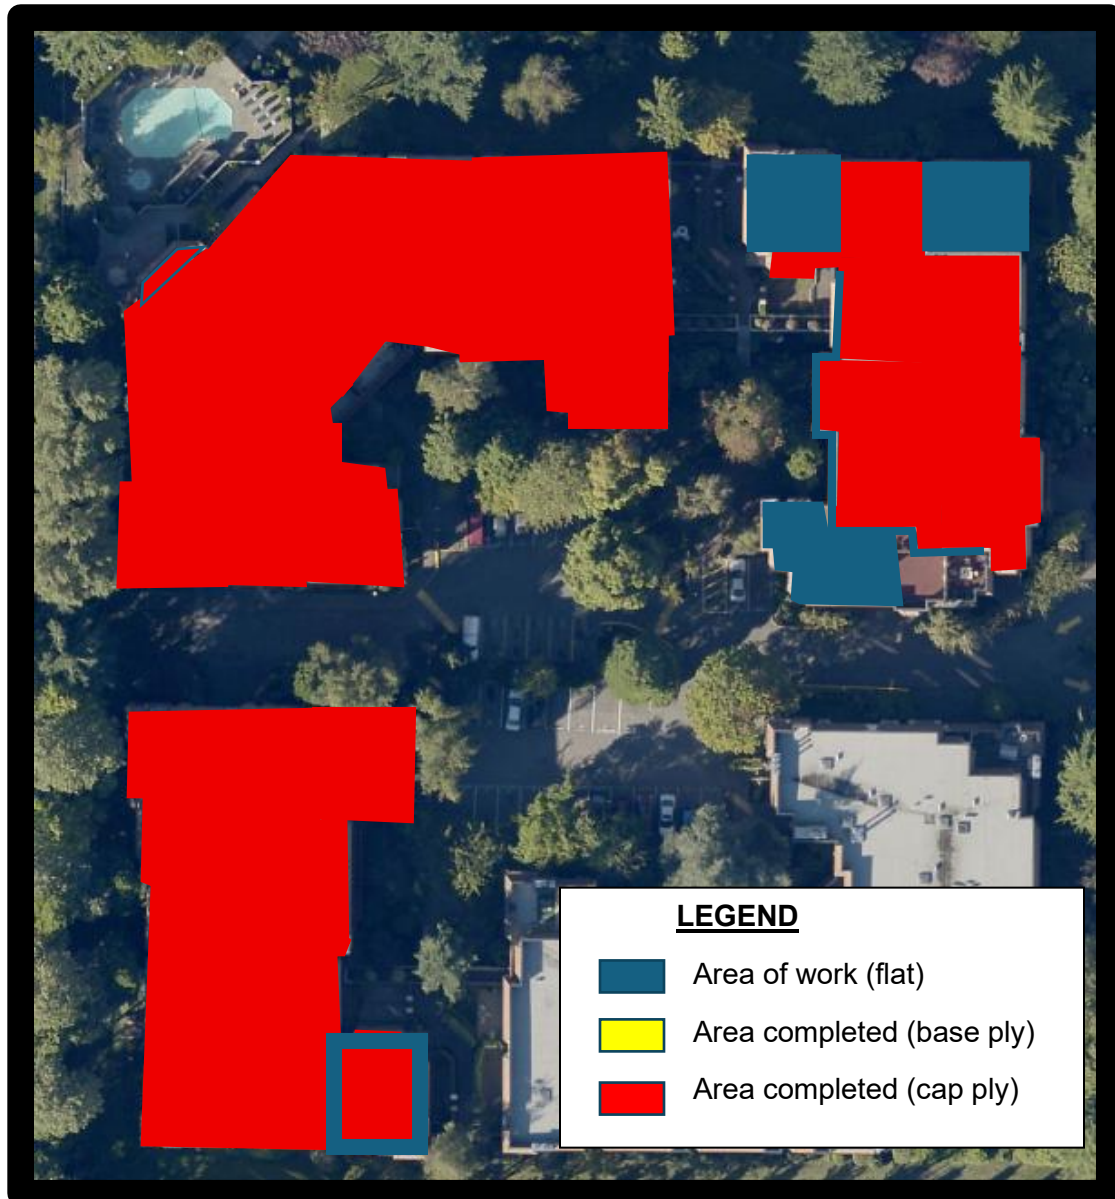

#### 24.1 **Building B**

Roofing is being cleaned and secured for the weekend.



#### 24.2 **Building C**

Incomplete adhesion in the base stripping has been corrected.



#### 24.3 **Building C**

Flashing installation is nearly completed, decking and privacy screen being reinstated.




#### 24.4 **Building C**

Flashing install and decking reinstatement continues on the noted deck.



#### 24.5 **Building A**

Preparation to the South decks has begun.

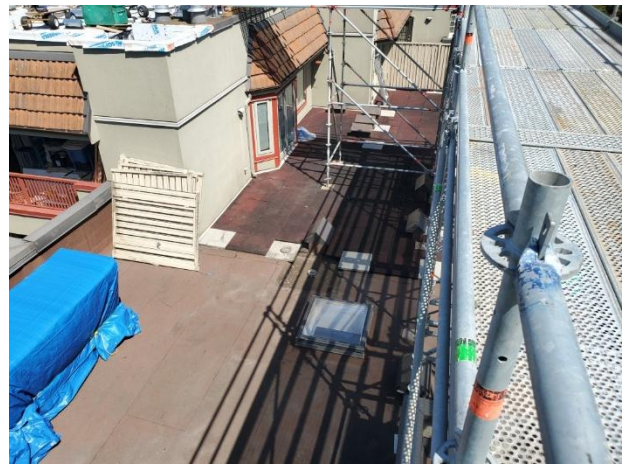

#### 24.6 **Building A**

The field application of Sopraply stick traffic cap has finished being applied to the main roof area.






#### 24.7 **Building A**

Membrane adhesion appears acceptable, and seam welded closed.



#### 24.8 **Building A**

An EF cement being applied to the edges of the field ply at the transitions for over the weekend due to cap stripping not yet installed.

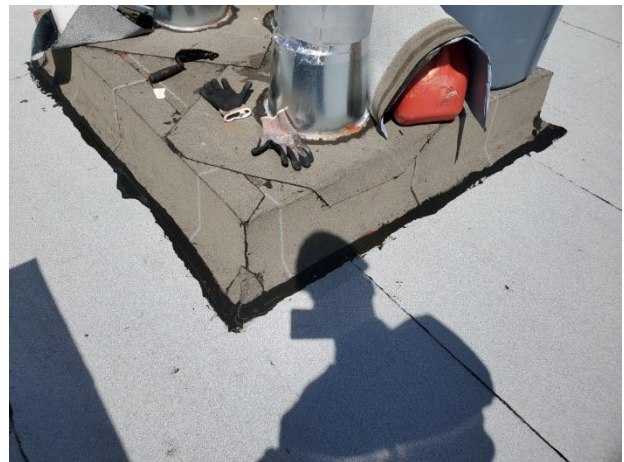

#### 24.9 **Building A**

In areas where cap stripping has been installed, adhesion appears acceptable.



24.10 **Building A**

Cap stripping laps onto the field 6" as required.



24.11 **Building A**

Alsan flashing install around the base of vents is in progress.



24.12 **Building A**

The application of 2n1 Smart Board sanded with 1/2" HD, Sopraply Stick DUO and 12" Sopra Lap has finished being applied to the Northwest deck area.

Seam welds appear acceptable.





24.13 **Building A**

2n1 board and 12" Sopra lap in progress of being installed.



24.14 **Building A**

Drain sumps are being created in an acceptable manner.



24.15 **Building A**

A nighttime seal being applied to perimeter of the field, until Densdek prime can be applied to the walls.



## **Outstanding Items:**

- N/A

Reported by:



**Matthew Blackstock, RRO**  
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
