




4611 Kelly Place
Delta BC
V4K 1G8
Tel: 604-317-3786
Email: ted@phoenixroofconsultants.ca

Installation Monitoring Report

Date: July 31, 2025

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number	53216
Address	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	Inspector	Matthew	Report Number	30
		Weather	Sun / 26°C	Time	1:15pm
Contractor	Flynn Canada Ltd.	Crew Size	16	Red Seal	6
				Apprentices	8

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

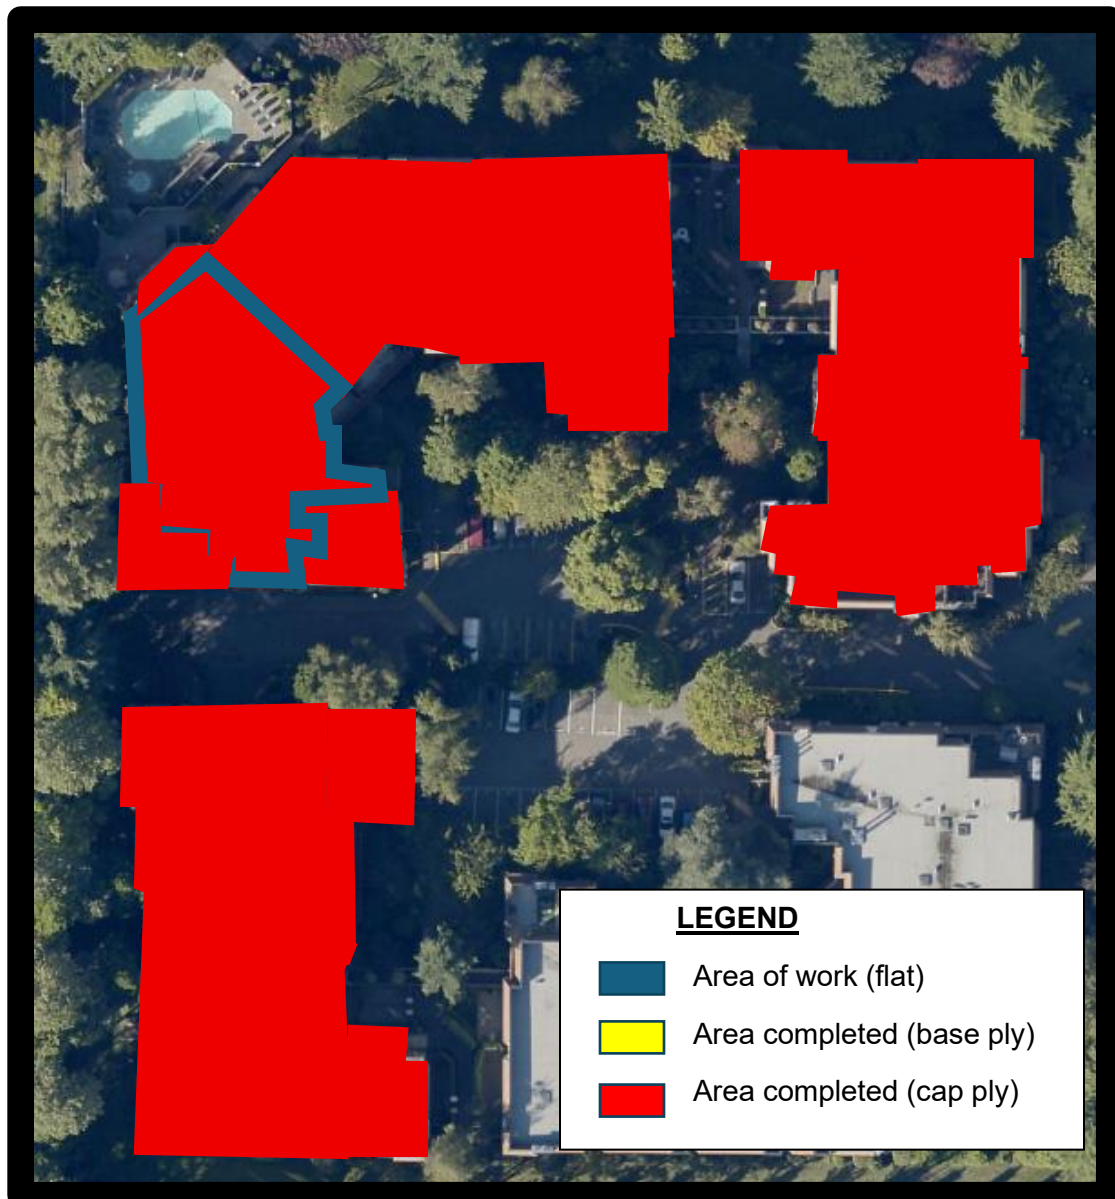

30.1 **Building C**

The crew are in process of cleaning up the roof area and final details are being applied.

Skylight install is expected to start next week.



30.2 **Building B**

The metal crew is working along the final section of the South parapet.



30.3 **Building B**

Exterior wind clips are being installed and secured to the face.



30.4 **Building B**

Hidden clips are being applied to the standing seam details, these must be 4" in length and have the required amount of pan head screws.




30.5 **Building A**

Metal flashing has begun to be loaded up to the roof area and non-essential equipment downloaded.



30.6 **Building A**

Rubber paver and privacy screen in progress of being reset in place.

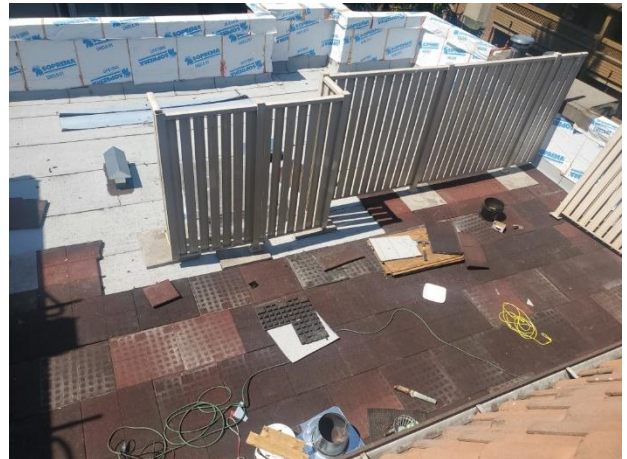

30.7 **Building A**

Previously noted open seam has been repaired in an acceptable manner.



30.8 **Building A**

Noted damage BUR vent hoods to be replaced with new.



Outstanding Items:

- N/A

Reported by:



Matthew Blackstock, RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
