




4611 Kelly Place
Delta BC
V4K 1G8
Tel: 604-317-3786
Email: ted@phoenixroofconsultants.ca

Installation Monitoring Report

Date: July 4, 2025

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number	53216
Address	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	Inspector	Matthew	Report Number	22
		Weather	Sun / 24°C	Time	2:00pm
Contractor	Flynn Canada Ltd.	Crew Size	22	Red Seal	6
				Apprentices	13

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

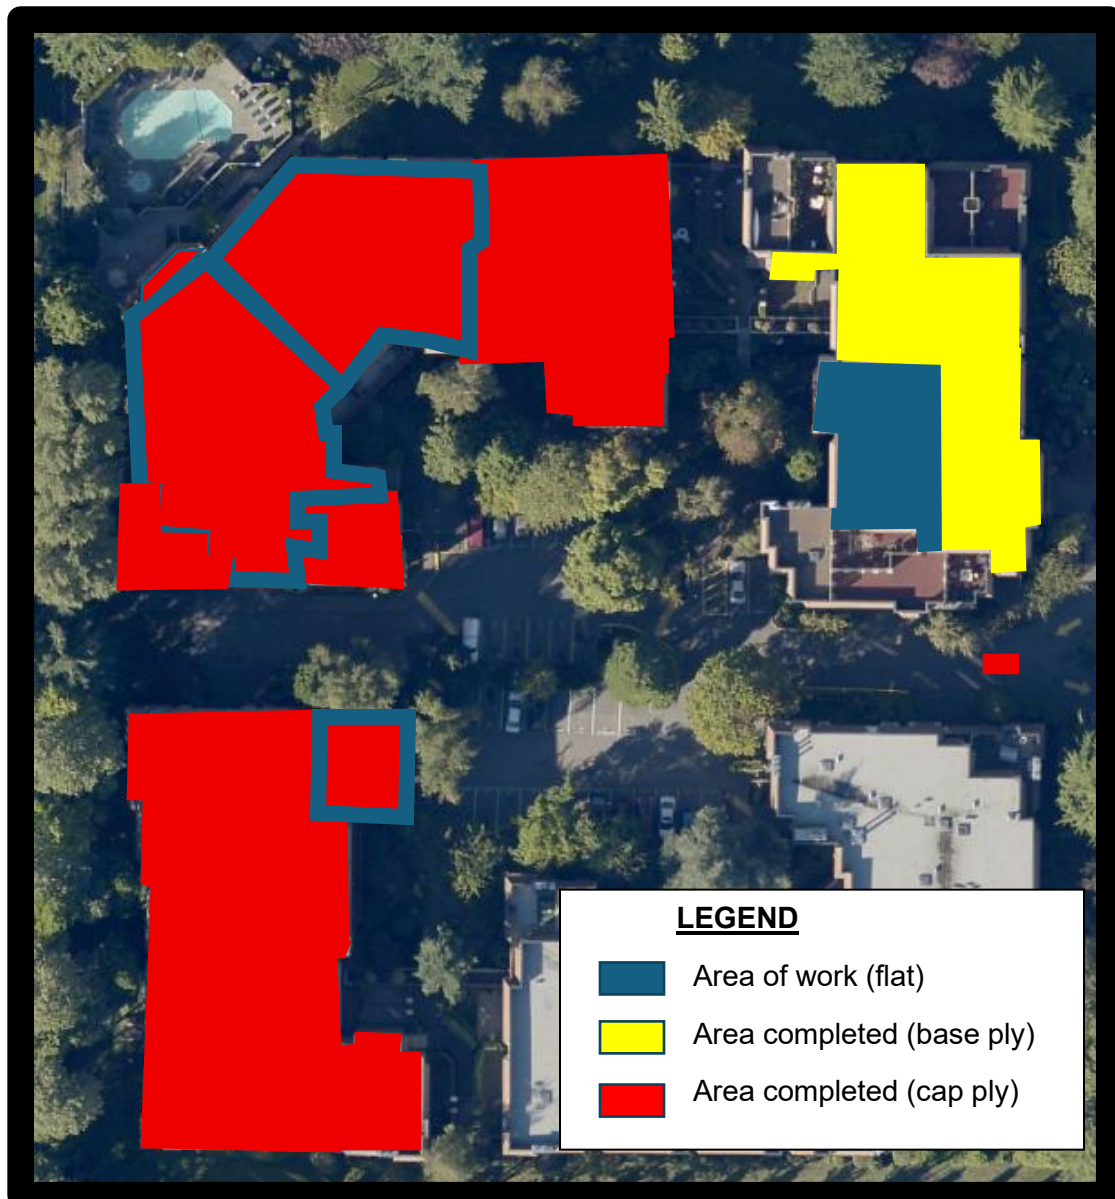

22.1 **Building B**

Overview of the roof, installation of the 24ga, pre-painted galvanized steel flashing continues to be installed to the parapets.



22.2 **Building B**

The double flashing detail continues to be installed to the top of the fire wall detail.



22.3 **Building B**

Correct S-lock details are being applied to corners and seams of the cross broken panels.



22.4 **Building C**

The installation of 26ga parapet flashing on the Northeast deck is underway.



22.5 **Building C**

The deck prime to be extended up to the vent strip opening and a 12" strip of Shield HT applied.



22.6 **Building C**


The overlay board is mechanically secured to the top of the parapet prior to install of the high temp self-adhering membrane.



22.7 **Building A**

Installation of the 2n1 smart board sanded with ½" HD ISO has finished being laid out over the pre-existing SBS adhered to the wood sheathing.

Foreman indicated that no deteriorated sheathing was found, and blisters were cut open prior to board install.

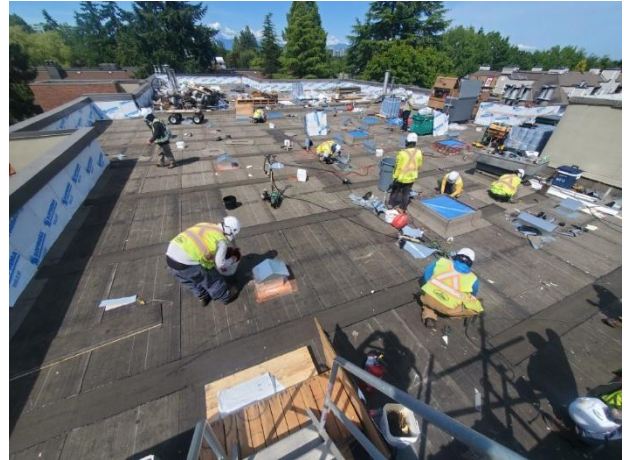


22.8 **Building A**

Sopraply DUO target patches have been created to be installed over the flanges of the BUR vents.



22.9 **Building A**

12" cover strips are being applied over the end joints of the 2n1 board in an acceptable manner.

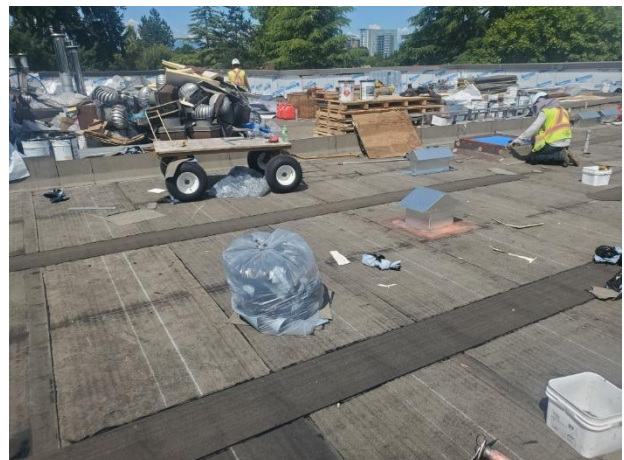


22.10 **Building A**

Laps and seams are welded closed once the membrane has been set in place.



22.11 **Building A**

Additional screws and plates with cover patch remain to be installed in some locations.

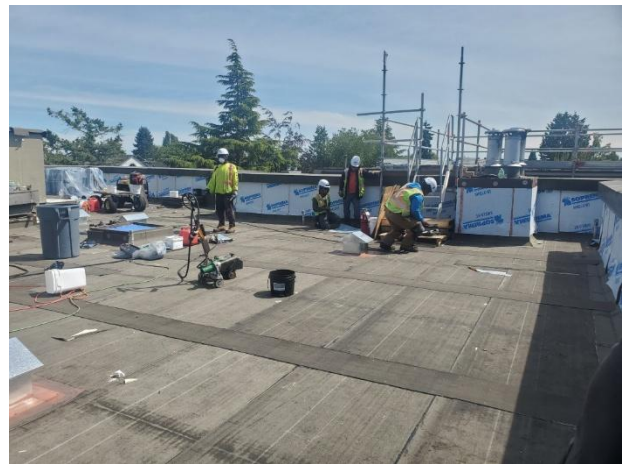

Outstanding Items:

- 16.3

Reported by:



Matthew Blackstock, RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
