




4611 Kelly Place
Delta BC
V4K 1G8
Tel: 604-317-3786
Email: ted@phoenixroofconsultants.ca

Installation Monitoring Report

Date: May 9, 2025

| | | | | | |
|-------------------|--|-------------------|----------|----------------------|---------|
| Project | NW 2050 Cypress Point | Job Number | 24064 | RGC Number | N/A |
| Address | 7511, 7531, 7651 Minoru Boulevard Richmond, B.C. | Inspector | Matthew | Report Number | 03 |
| | | Weather | Sun/16°C | Time | 12:30pm |
| Contractor | Flynn Canada Ltd. | Crew Size | 9 | Red Seal | 3 |
| | | | | Apprentices | 5 |

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

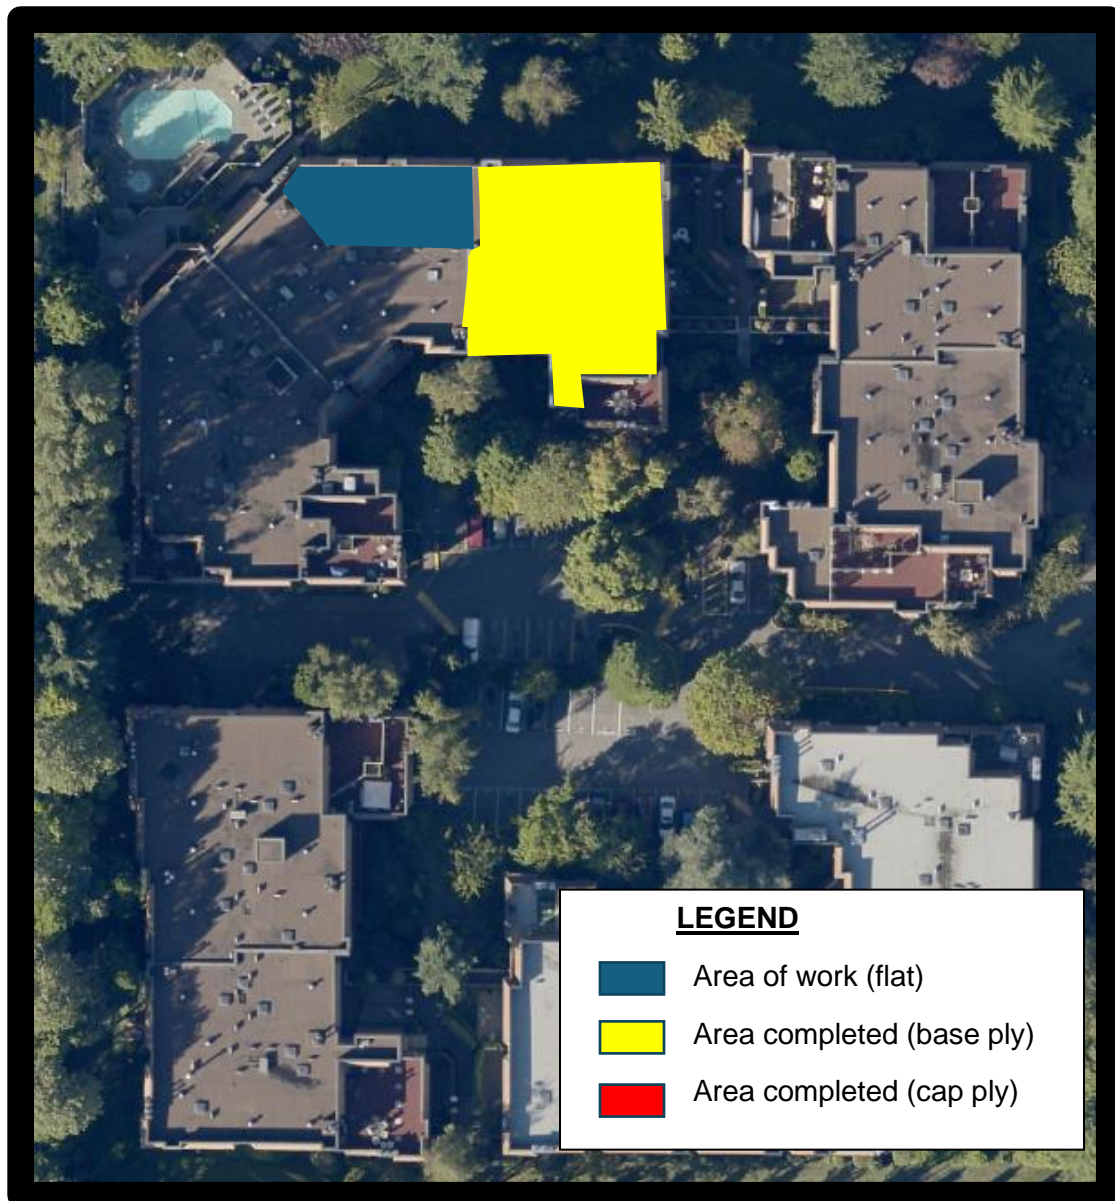

3.1 **Building B**

Crew have begun to lay out the Soprema 2n1 smartboard sanded with ½" HD ISO board along the North side on the center section of the roof.




3.2 **Building B**

Overlay board is being secured with the 2" Barded seam plates and 2" #14 dek fast screws to the wind uplift pattern provided by the material manufacturers application instructions.



3.3 **Building B**

End joints are butted together and primed with an Elastocol adhesive stick primer to allow for 12" sopra lap to be applied.

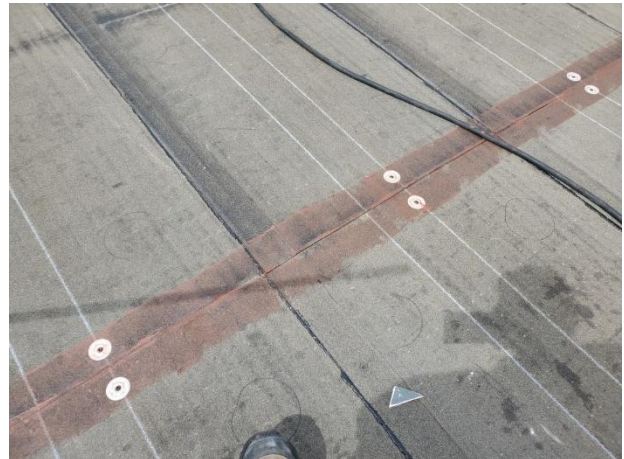

3.4 **Building B**

Seams are being heat welded closed with robot and held welders.



3.5 **Building B**

Sopraply stick DUO is being rolled into primed surfaces and seams welded closed.

Adhesion appears acceptable.



3.6 **Building B**

Multiple protrusion details are being worked on as per specifications.




3.7 **Building B**

In the East roof section, protrusion details are being worked on.



3.8 **Building B**

Aluminum pipe flashing is being fitted around the plumbing exhaust vents and roofed in with a patch of Sopraply stick DUO membrane.

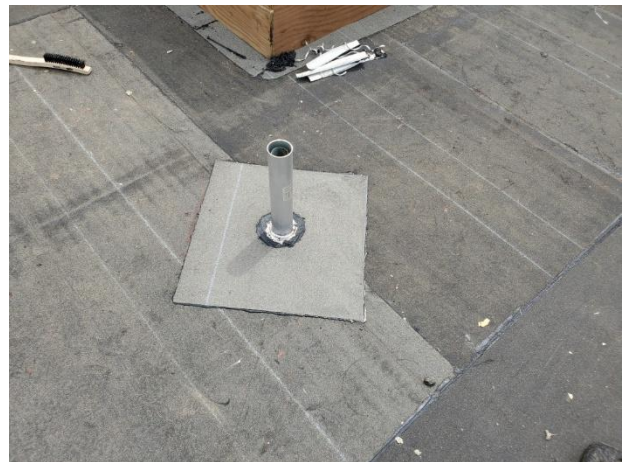

3.9 **Building B**

BUR vents are being applied around the dryer exhaust vents, insulation and vent details remain to be completed.



3.10 **Building B**

A 3' x 3' drain sump is being created prior to 3" spun copper clamping drains are being installed.

Foreman indicated the Furnco mechanical connections are in place at the outflow pipe.



3.11 **Building B**

Previously noted deflection at the curb detail has been corrected.



Outstanding Items:

- None currently.

Reported by:

A handwritten signature in black ink, appearing to read 'Matthew Blackstock', with a stylized flourish at the end.

Matthew Blackstock, RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
