




4611 Kelly Place
Delta BC
V4K 1G8
Tel: 604-317-3786
Email: ted@phoenixroofconsultants.ca

Installation Monitoring Report

Date: August 22, 2025

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number	53216
Address	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	Inspector	Matthew	Report Number	37
		Weather	Sun / 25°C	Time	12:40pm
Contractor	Flynn Canada Ltd.	Crew Size	8	Red Seal	2
				Apprentices	3

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

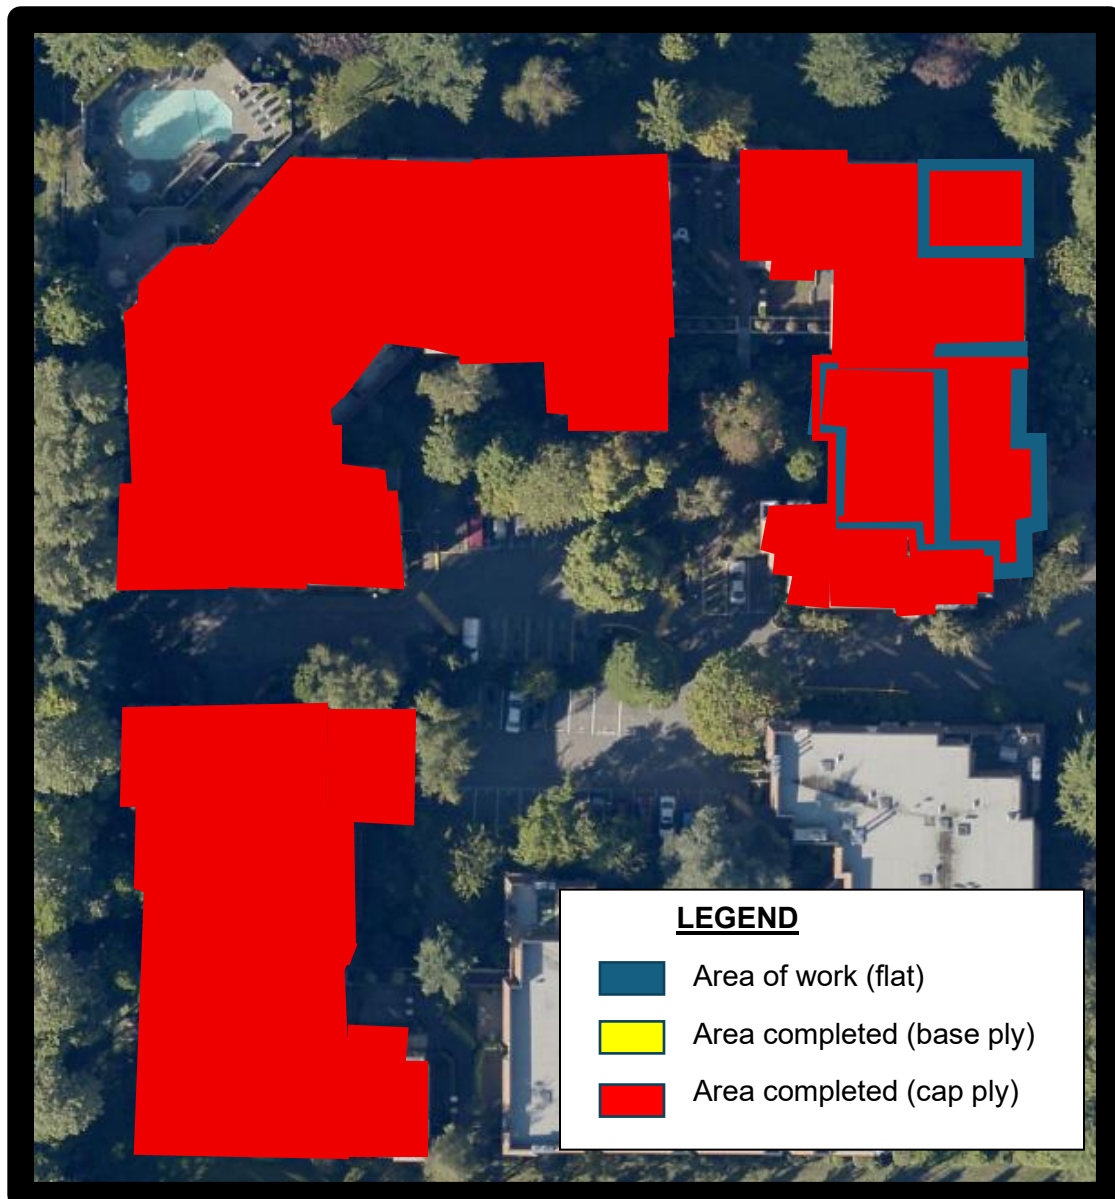


37.1 **Building A**

The installation of the cross broken panels is underway to the parapet walls.



37.2 **Building A**

S-lock details applied to the corners and integrated at seams. Securement with pan head screws appears acceptable.

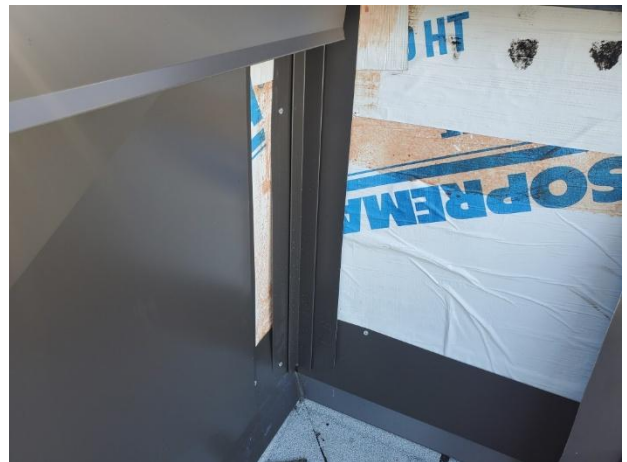

37.3 **Building A**

Cap flashing install with a continuous wind clip is underway. Stand offs to allow for opening strips remain to be applied.




37.4 **Building A**

Panels have finished being applied to the Northwest deck area, cap flashing remains to be installed.




37.5 **Building A**

Scupper remaining to be sealed to the exterior stucco and downpipe attachment to be installed.

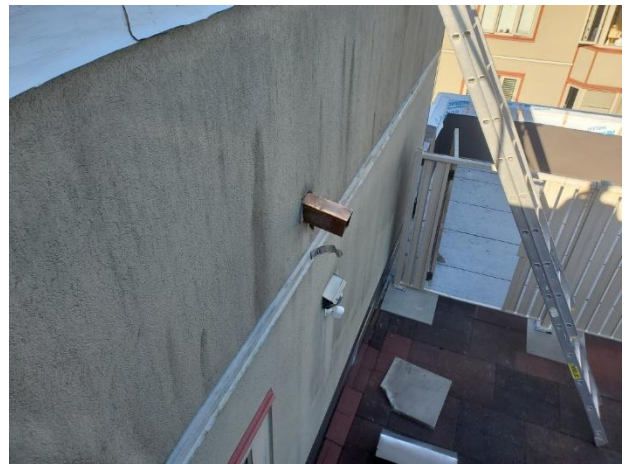

37.6 **Building A**

Chimney chase details continue to be worked on.

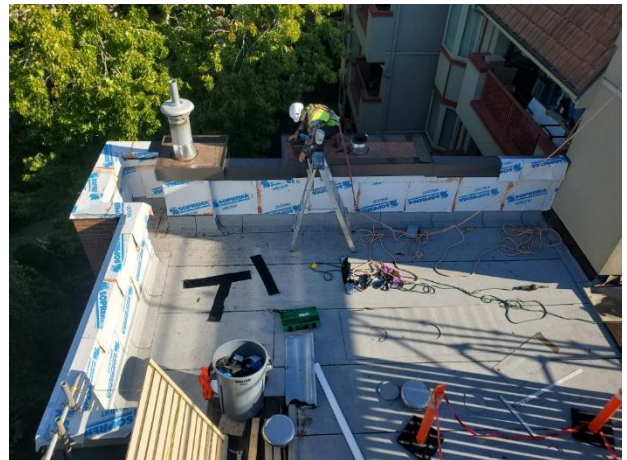

Outstanding Items:

- Items #34.6 – 34.8

Reported by:



Matthew Blackstock, RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
