




4611 Kelly Place
Delta BC
V4K 1G8
Tel: 604-317-3786
Email: ted@phoenixroofconsultants.ca

Installation Monitoring Report

Date: July 15, 2025

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number	53216
Address	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	Inspector	Matthew	Report Number	25
		Weather	Sun / 29°C	Time	1:30pm
Contractor	Flynn Canada Ltd.	Crew Size	13	Red Seal	5
				Apprentices	14

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

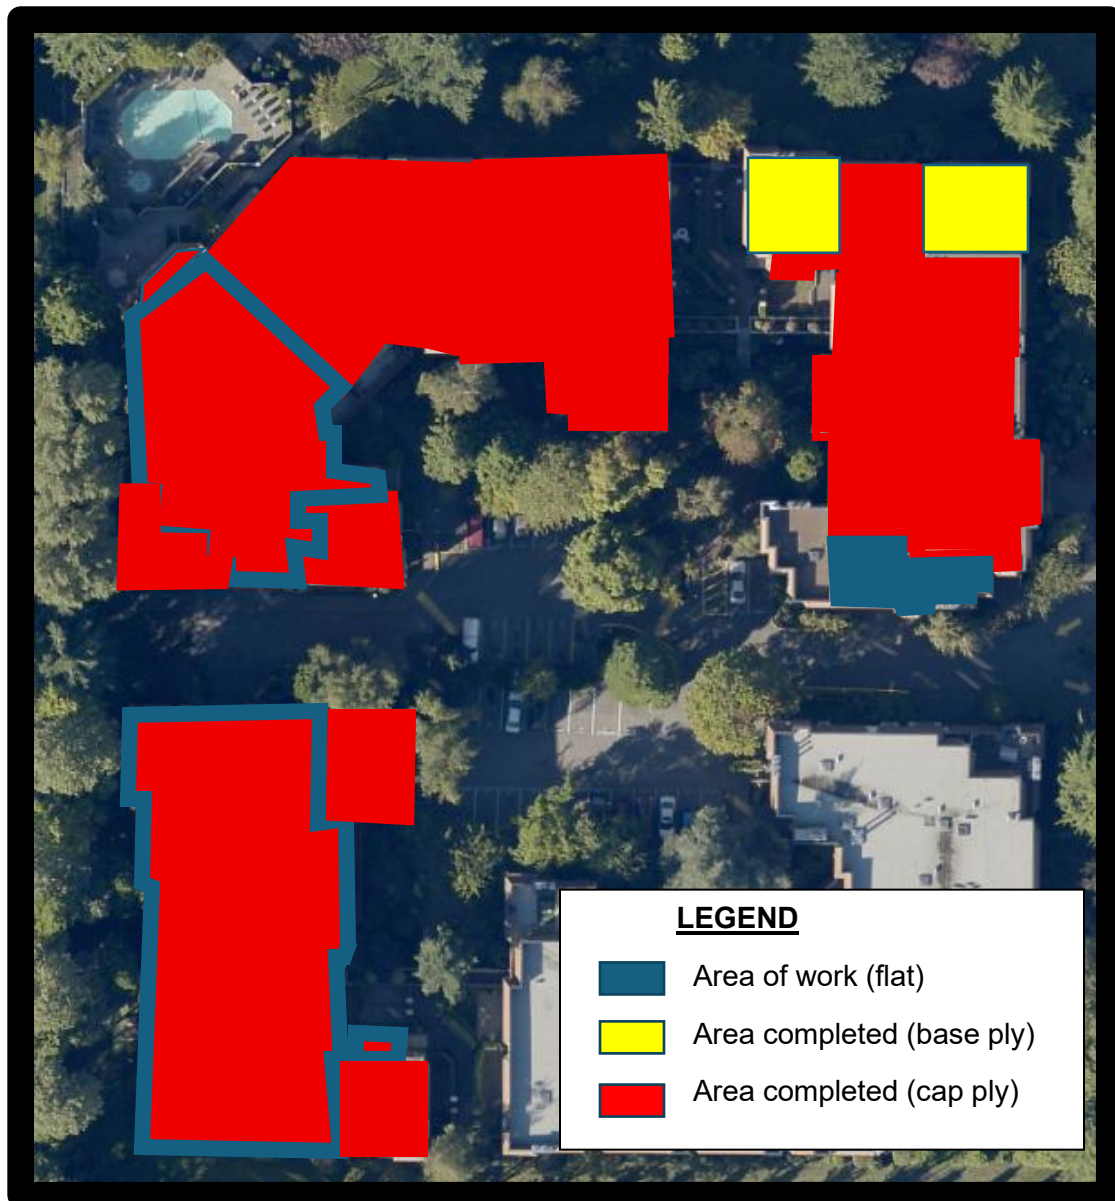


25.1 **Building C**

Installation of flashing details is in progress along the noted buildings parapets.



25.2 **Building C**

A continuous 24ga wind clip is in progress of being applied and secured in place with pan head screws 12" OC on the top and front face.

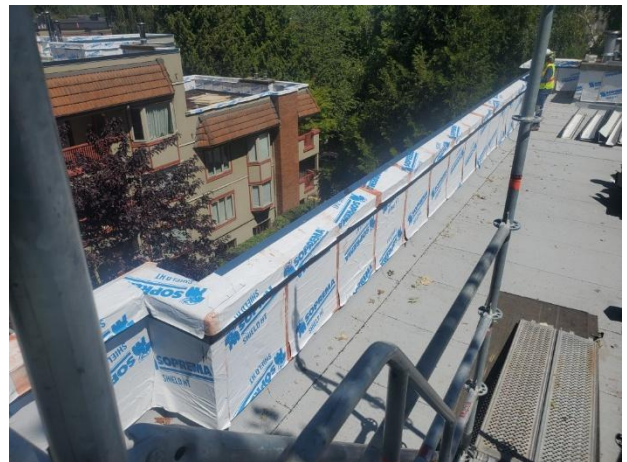

25.3 **Building C**

Saddle to chimney details in progress of being applied.




25.4 **Building C**

The gravel stop details are being applied to the sides and top of the chimney details.



25.5 **Building A**

Overview of the work area on the South deck area.

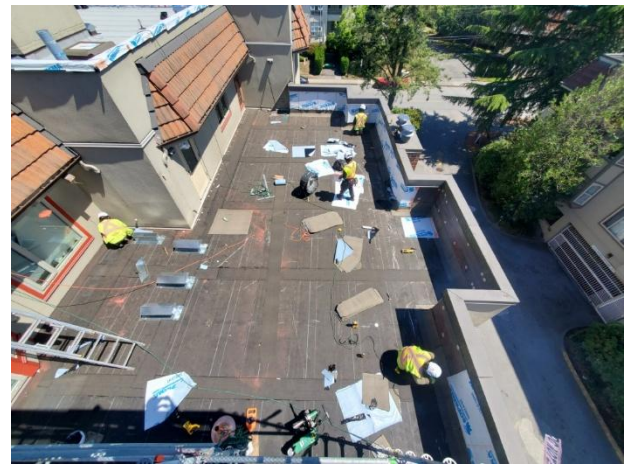

25.6 **Building A**

The field application of the 2n1 Smartboard with ½" HD board is being laid out and secured with 2" barbed seam plates and 2" dek fast screws.



25.7 **Building A**

The side laps and 12" cover strip welds appear acceptable.




25.8 **Building A**

Sopraply Stick DUO has been rolled into the Elastocol stick adhesive primer and seams welded closed.



25.9 **Building A**

Shield HT is being rolled on to Elastocol stick primed surface of the mech attached densdeck prime overlay on the parapets.

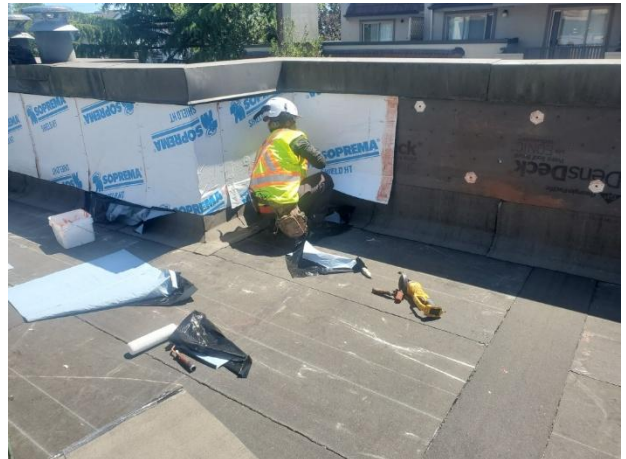


25.10 **Building A**

Installation of the base layer is near completed to the Northeast deck location.



25.11 **Building A**

Noted lifting overlay board in the drain sump to be corrected.

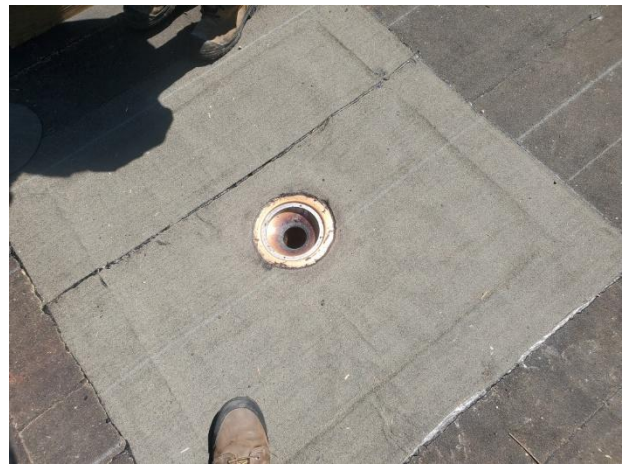

25.12 **Building A**

The application of 2n1 Smartboard sanded with 1/2" HD, Sopraply Stick DUO and 12" Sopra Lap has finished being applied to the Northwest deck area.

Seam welds appear acceptable.



25.13 **Building A**

Crew working on membrane tie-in at the parapet to wall detail.



25.14 **Building A, Unit 307**


The indicated leak location that occurred in the noted unit last Wednesday rain fall.

Tape marks indicated locations of moisture that were recorded by another contractor.



25.15 **Building A, Unit 307**

Infrared scans of the area show temperature differentials that can indicate moisture still present.

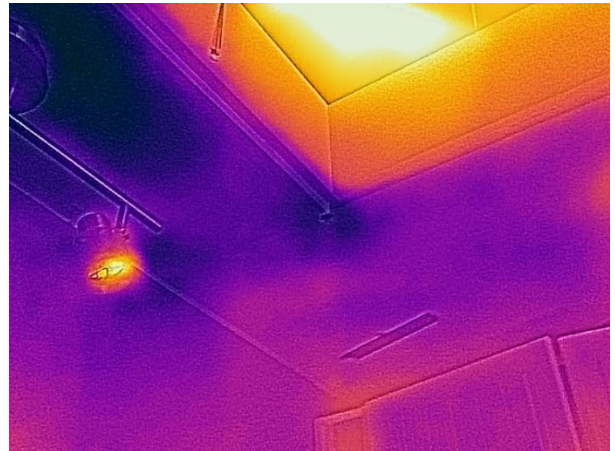

25.16 **Building A, Unit 307**

The cause of the leak was from a compromised temporary seal on the skylight, which has now been repaired.

Flynn Canada to provide schedule of installation of the dehumidifier within the unit and timings of repairs.



Outstanding Items:

- N/A

Reported by:



Matthew Blackstock, RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
