




4611 Kelly Place  
Delta BC  
V4K 1G8  
Tel: 604-317-3786  
Email: ted@phoenixroofconsultants.ca

## Installation Monitoring Report

Date: June 5, 2025

<b>Project</b>	NW 2050 Cypress Point	<b>Job Number</b>	24064	<b>RGC Number</b>	53216
<b>Address</b>	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	<b>Inspector</b>	Matthew	<b>Report Number</b>	12
		<b>Weather</b>	Sun / 18°C	<b>Time</b>	8:35am
<b>Contractor</b>	Flynn Canada Ltd.	<b>Crew Size</b>	13	<b>Red Seal</b>	4
				<b>Apprentices</b>	6

**Distribution List:** keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

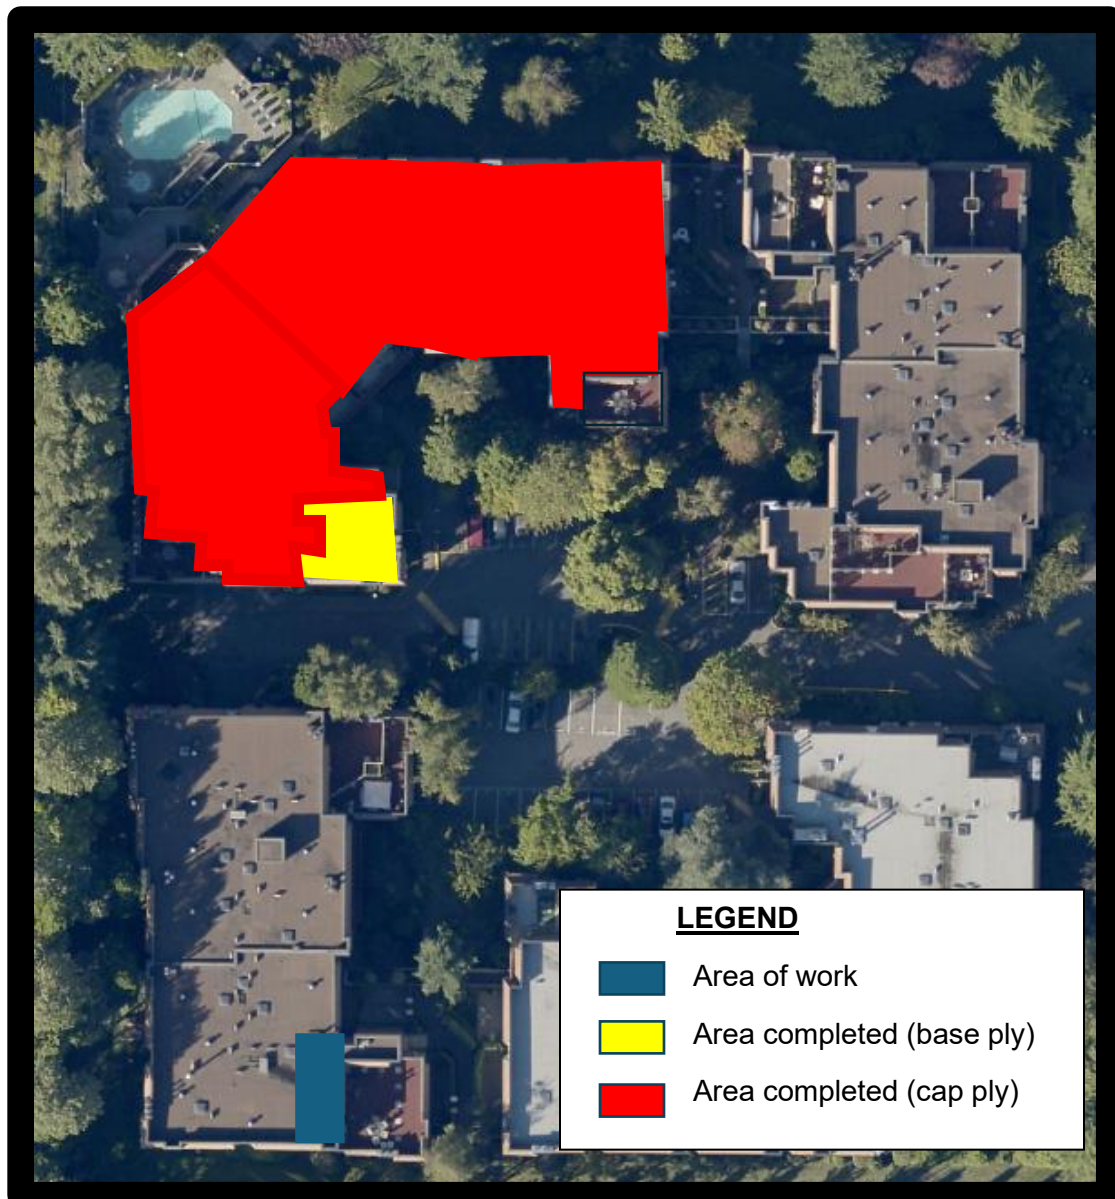

12.1 Staging area is clean and organized.




## 12.2 **Building B**

Southeast deck is now complete with the base ply. Noted wrinkled target patch at the drain- foreman indicated this was temporary as the drain needs to be pulled and connected.



## 12.3 **Building B**

Target patches at vents have been kept back from the vertical upstand by 1" to allow for the cap ply to bond to the flange as well, creating a double seal.

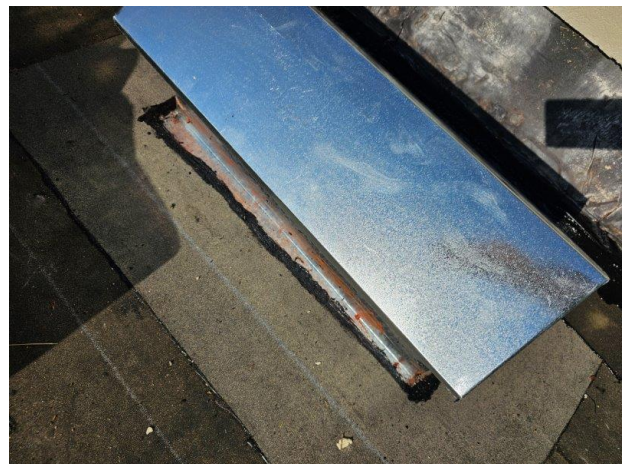



#### 12.4 **Building B**

Numerous wrinkles were noted in the stripping plies. The membrane must be installed as smoothly as possible without wrinkles.




#### 12.5 **Building B**

It was noted that the stripping plies are sealed where they overlap with no small openings noted.



#### 12.6 **Building B**

Crew have achieved sufficient bleed out with the base ply side laps.

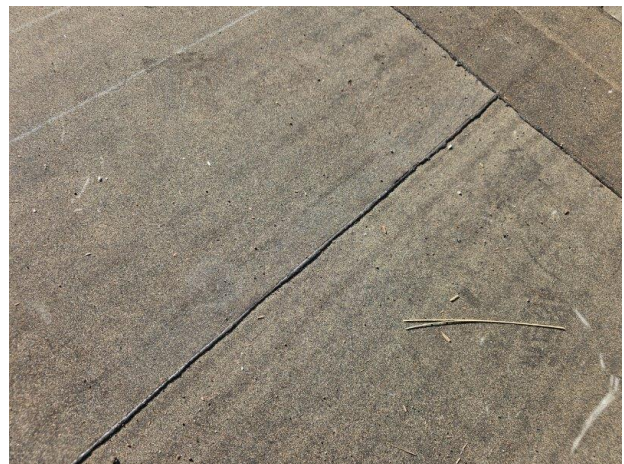

### 12.7 **Building B**

Sopralap has been installed over the end laps of the 2n1 Soprasmart Board ISO+ Sand.



### 12.8 **Building B**

Walls at the deck are protected with Soprema Shield HT.



### 12.9 **Building B**

It appears that personal belongings are still remaining to be removed from the deck on Unit 312.





#### 12.10 **Building C**

Crew are working at the Southeast area noted on the roof plan above.




#### 12.11 **Building C**

The existing membrane has had blisters and buckles cut out in the work area and was reported to have been cleaned. 2n1 Soprasmart Board ISO+ Sand has been laid out.



#### 12.12 **Building C**

Crew are installing DensDeck Prime to the parapets.

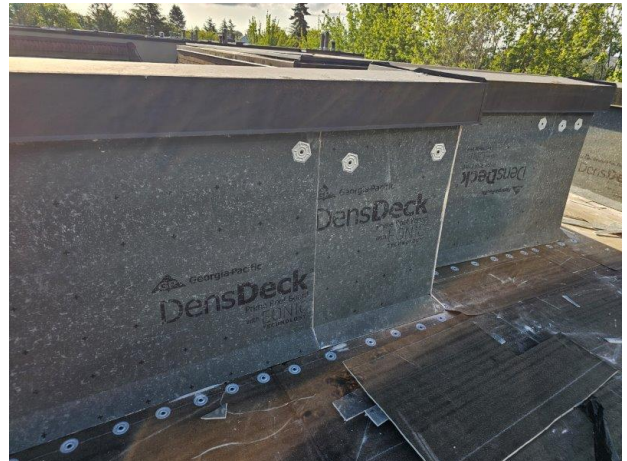

### 12.13 **Building C**

Membrane plates and #14E-coated screws are being installed. It was observed that the crew are not overtightening the fasteners which would result in depressions in the ISO.



### 12.14 **Building C**

Material has been covered with tarps to protect from the weather as required.



## **Outstanding Items:**

- 8.7, 9.3, 9.4, 9.5, 10.3

Reported by:



**Matthew Blackstock, RRO**  
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
