




4611 Kelly Place  
Delta BC  
V4K 1G8  
Tel: 604-317-3786  
Email: ted@phoenixroofconsultants.ca

## Installation Monitoring Report

Date: May 27, 2025

<b>Project</b>	NW 2050 Cypress Point	<b>Job Number</b>	24064	<b>RGC Number</b>	53216
<b>Address</b>	7511, 7531, 7651 Minoru Boulevard Richmond, B.C.	<b>Inspector</b>	Matthew	<b>Report Number</b>	08
		<b>Weather</b>	Sun / 17°C	<b>Time</b>	1:30pm
<b>Contractor</b>	Flynn Canada Ltd.	<b>Crew Size</b>	11	<b>Red Seal</b>	4
				<b>Apprentices</b>	6

**Distribution List:** keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

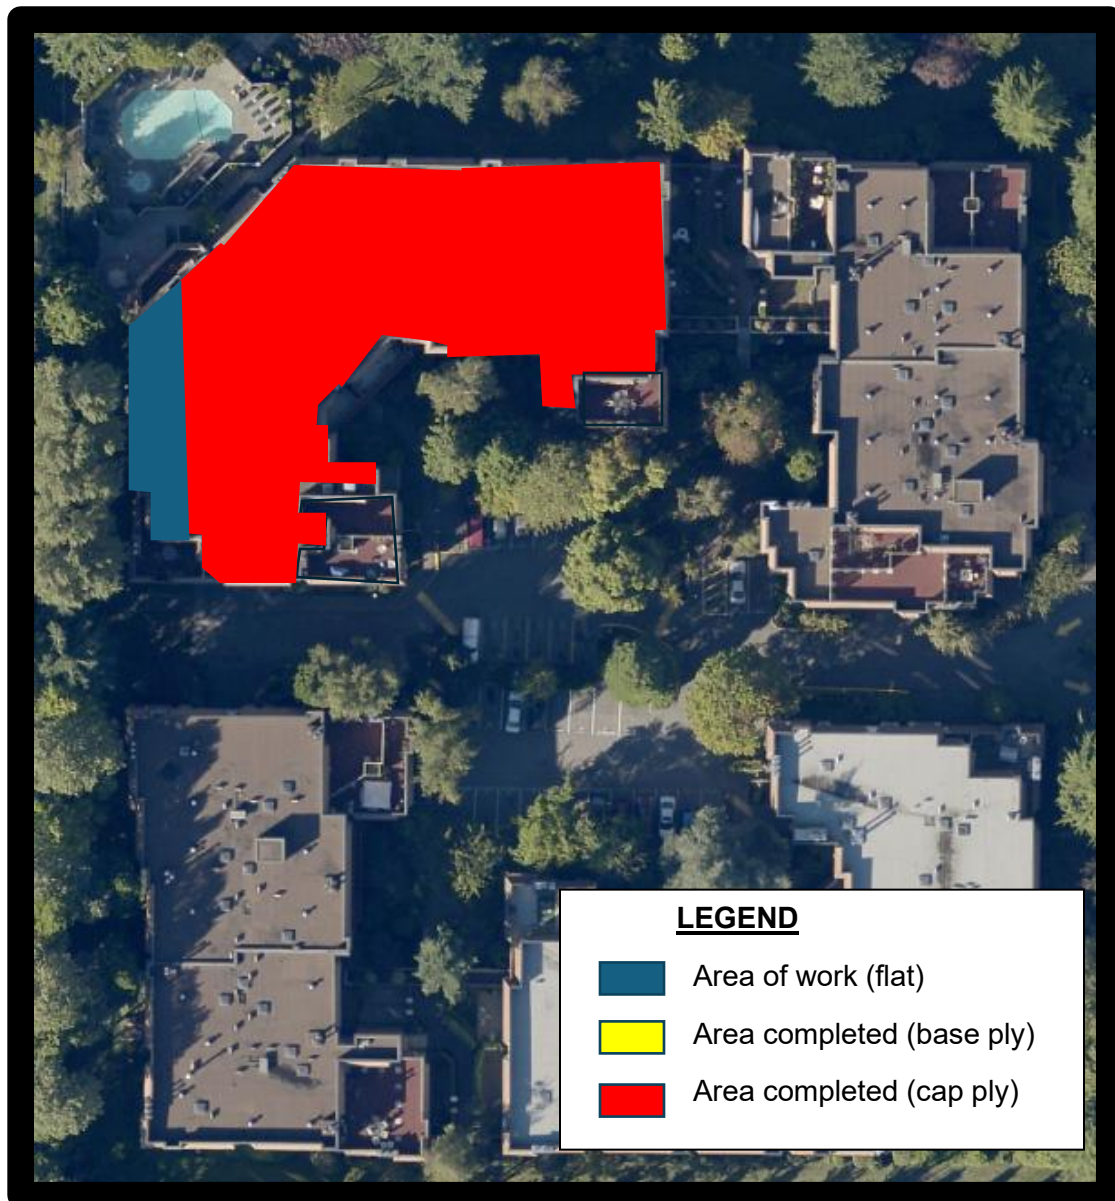


### 8.1 **Building B**

Installation of the Sopraply stick Traffic Cap is 85% complete being applied to the main roof area.




### 8.2 **Building B**

Noted cap roll offset from the base layer side lap is found at 14" - 18", this is acceptable.

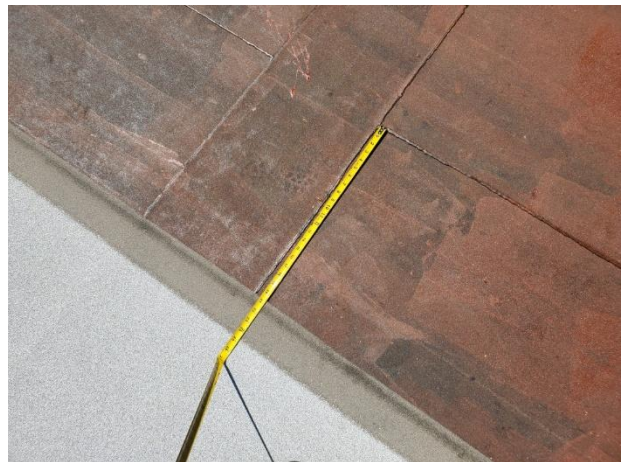

### 8.3 **Building B**

The cap field membrane adhesion to the 2n1 smart board sanded with Elastocol stick adhesive primer appears acceptable.

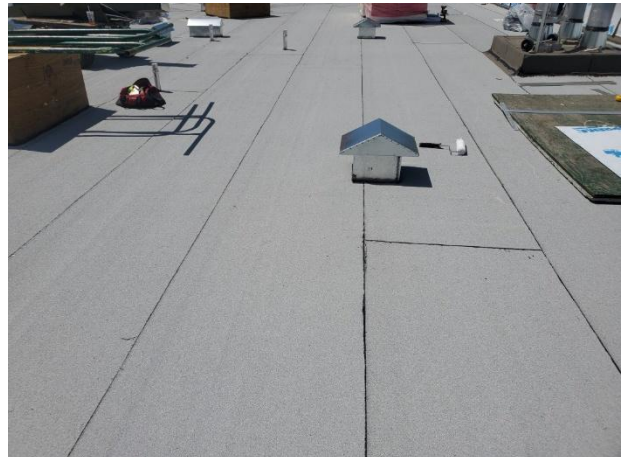



#### 8.4 **Building B**

Previously noted field application deficiencies have been corrected to membrane manufacturers requirements.



#### 8.5 **Building B**

Independent cap stripping has begun on the East wing of the building.



#### 8.6 **Building B**

The cap stripping laps on to the field the 6" as required and seams appear welded closed.



### 8.7 **Building B**

One small incomplete adhesion was noted and marked for repair.



### 8.8 **Building B**

Due to the old SA membrane not being able to be removed on the top of the parapet, asphalt overlay board is being applied prior to a new HT SA membrane being applied.



### 8.9 **Building B**

Slices in the HT SA membrane to be repaired.





#### 8.10 **Building B**

New Dayliter skylight on site being dry fitted to the curbs.



#### 8.11 **Building B**

The additional 2 x 2 buildup remains to receive the approved membrane installation.



#### 8.12 **Building B**

The 24ga parapet flashing mockup was reviewed with Foreman.




8.13 **Building B**

The cross broken panels must overlap the head of the base wall flashing 4" and the base flashing kept 1" off the roof surface.




8.14 **Building B**

Double S-locks must be applied at all vertical panel seams. Panels must be no larger than 4' wide.

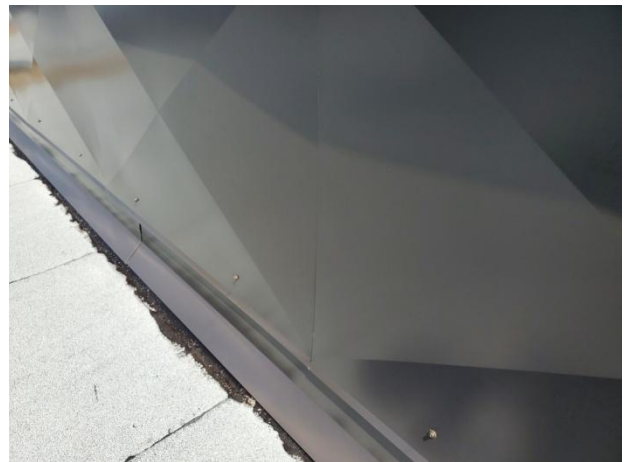

8.15 **Building B**

The perforated vent strip detail found acceptable.

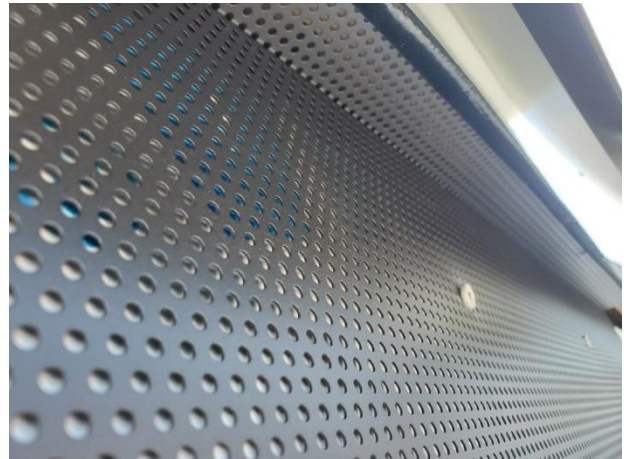

8.16 **Building B**

A continuous wind clip is acceptable.



8.17 **Building B**


An RCABC fire wall flashing detail are to be applied along the two locations on the main roof.



## **Outstanding Items:**

- None currently.

Reported by:

A handwritten signature in black ink, appearing to read 'Matthew Blackstock', with a stylized flourish at the end.

**Matthew Blackstock, RRO**  
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
