

Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		N/A	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report Number		02	
	Richmond, B.C.	Weather	Sun / 15°C	Time		1:30pm	
Contractor	Flynn Canada Ltd.	Crew Size	9 Red Seal	3	Apprent	ices	5

Date: May 7, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca




2.1 **Building B**

Crew are continuing to work on the East side of the noted building.



2.2 **Building B**

Robot hot air welder is being used to weld the seams of the 2n1 smartboard. This is acceptable.



2.3 **Building B**

Temperature settings reviewed.



2.4 **Building B**

Roofing contractor to fix gaps noted in the smart board ½" board.



2.5 **Building B**

Sopraply Stick DUO base stripping application is being rolled into Elastocol primed surfaces and seams are hot air welded closed.



2.6 **Building B**

The parapet walls are receiving high temp as per specifications.



2.7 **Building B**

The 12" Sopralap is being welded over the end joints as required.




2.8 **Building B**

Cover patch over the new BUR vents are being applied in an acceptable manner.



2.9 **Building B**

Aluminum pipe flashing has begun to be installed around the plumbing pipes.

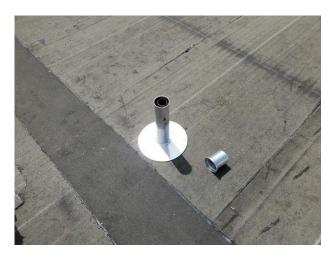

2.10 **Building B**

Drains temporarily sealed in place until the 3'x3' sump can be created.



2.11 **Building B**

Fan and conduit details remain to be temporarily disconnected to be roofed in.



Outstanding Items:

• None currently.

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
